



ELECT MAINT Department
SIMHADRI

Note No :1



Ref:SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

Date:11/09/2023(17:58:33)

Subject:LMI on CAPACITY TESTING OF DC BATTERIES

LMI on capacity testing of DC batteries is modified as per the LMI/OD/OPS/ELEC/004-CAPACITY TESTING OF DC NI-CD BATTERIES.

The new revision is approved based on COS-ISO-00-OD/OPS/ELEC/004 Rev. No.: 02 July 2023

Accordingly modified LMI is proposed with the following changes.

- The capacity test of battery banks should be carried out every 2 years with unit overhauling, earlier frequency of capacity testing was annually in Rev-1
- Annexure-V Help document for uploading battery capacity test data in SAP
- Annexure I,II,III modified as per new OD

put up for approval.

Submitted by:

बाला बालाजी आकुला - उप महाप्रबंधक

BALA BALAJI AKULA - 009145 (DY. GENERAL MANAGER ,ELECT MAINT) ,Simhadri
(ABALABALAJI@NTPC.CO.IN, 8332959245)

On:11/09/2023(17:58:33) **Ref:**SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

Note No:2

Submitted by:

तेन्नेटि विजय कृष्ण - अपर महाप्रबंधक

Tenneti Vijay Krishna - 007966 (ADDL. GENERAL MANAGER ,ELECT MAINT)
(TVIJAYKRISHNA@NTPC.CO.IN, 9437188892) ,Simhadri

On:13/09/2023(18:32:13) **Ref:**SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

Note No:3

Submitted by:

बाला बालाजी आकुला - उप महाप्रबंधक

BALA BALAJI AKULA - 009145 (DY. GENERAL MANAGER ,ELECT MAINT)
(ABALABALAJI@NTPC.CO.IN, 8332959245) ,Simhadri

On:14/09/2023(10:54:13) **Ref:**SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

Note No:4

LMi reviewed and found in order

Submitted by:

धर्मेन्द्र कुमार तोमर - अपर महाप्रबंधक

Dharmendra Kumar Tomar - 007286 (ADDL. GENERAL MANAGER ,ELECT MAINT)
(DHARMENDRAKUMAR02@NTPC.CO.IN, 9416212079) ,Simhadri

On:14/09/2023(20:01:50) **Ref:**SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

Note No:5

Submitted by:

ऊमा शंकर वर्मा - अपर महाप्रबंधक

Uma Shanker Verma - 006137 (ADDL. GENERAL MANAGER ,EEMG)
(USVERMA@NTPC.CO.IN, 9650992821) ,Simhadri

On:15/09/2023(09:12:13) **Ref:**SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

Note No:6

Submitted by:

अजय गुप्ता - उप महाप्रबंधक

Ajay Gupta - 008565 (DY. GENERAL MANAGER ,EEMG)
(AJAYGUPTA04@NTPC.CO.IN, 9958105993) ,Simhadri

On:15/09/2023(09:14:59) **Ref:**SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

Note No:7

LMI reviewed and forwarded for further approval

Submitted by:

टी.आर. राजगोपालन् - महाप्रबंधक

TR Rajagopalan - 003994 (GENERAL MANAGER ,OPERATION)
(TRRAJAGOPAL@NTPC.CO.IN, 9440918024) ,Simhadri

On:15/09/2023(09:50:17) **Ref:**SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

Note No:8

Submitted by:

मैथ्यू ई कोवूर - महाप्रबंधक

Mathew Eipe Kovoor - 005637 (GENERAL MANAGER ,MAINTENANCE)
(MEKOVOOR@NTPC.CO.IN, 9650994652) ,Simhadri

On:16/09/2023(12:10:47) **Ref:**SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

Note No:9

May please approve

Submitted by:

धुरजति प्रसाद पात्रा - महाप्रबंधक

Dhurjati Prasad Patra - 004573 (GENERAL MANAGER ,O & M)
(DPPATRA@NTPC.CO.IN, 8275045446) ,Simhadri

On:17/09/2023(23:52:49) **Ref:**SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

Note No:10

Approved & Submitted by:

संजय कुमार सिन्हा - महाप्रबंधक

Sanjay Kumar Sinha - 005185 (GENERAL MANAGER ,HEAD OF PROJECT)
(SKSINHA06@NTPC.CO.IN, 9431215239) ,Simhadri

On:18/09/2023(17:36:51) **Ref:**SMTPP/ELECT MAINT/2023-24/EMLMICAP/475001

NTPC Limited

SIMHADRI SUPER THERMAL POWER PROJECT

LMI/OD/OPS/ELEC/004
ISSUE NO: 1, REVISION: 2
DATE: JULY 2023

CAPACITY TESTING OF DC NI-CD BATTERIES

APPROVED FOR
IMPLEMENTATION BY - - - - -
HEAD OF THE PROJECT (SIMHADRI)

Date: _____

NTPC Limited
SIMHADRI SUPER THERMAL POWER STATION
OPERATION & MAINTENANCE DEPARTMENT

LMI (Name): CAPACITY TESTING OF DC NI-CD BATTERIES			
LMI No. : LMI /OD/OPS/ELEC/004			
Issue No.	1	Revision : 2	Date: JULY 2023

	Name	Designation	Signature
Prepared by	Balabalaji Akula	DGM(EM)	
Verified by	T. VIJAY KRISHNA	AGM(EM)	
Verified by	D.K. TOMAR	AGM (EM) I/C	
Verified by	G. HARI NARAYANA RAO	AGM (C&I) I/C	
Verified by	MATTHEW EIPE KOVOOR	GM(Maint)	
Reviewed by	D.P. PATRA	GM(O&M)	

CAPACITY TESTING OF DC NI-CD BATTERIES

SL.NO.	CONTENTS	PAGE NOS.
01	INTRODUCTION	3
02	SUPERCEDED DOCUMENTS	3
03	SCOPE	3
04	REFERENCE DOCUMENT	3
05	REVISION DETAILS	3
06	PROCEDURE	4-7
07	RESPONSIBILITIES	7
08	DOCUMENTS	8
09	EXCEPTION REPORTING & DESPENSATION	9
10	REVIEW	9

CAPACITY TESTING OF DC NI-CD BATTERIES

1. INTRODUCTION :

The DC power supply is of vital importance for the safety & security of the power station. At Simhadri Ni-Cd batteries are used for main plant, Switchyard and Make up water Pump houses. The ampere hour capacity of the batteries is to be assessed regularly. In general the AH capacity of the batteries decreases with service life & rate of degradation depends on ambient & service temperature, maintenance practices. This capacity test will help to assess the actual bank capacity available at the time of the test & to identify the weak cells and take suitable corrective action.

2. SUPERCEDED DOCUMENTS:

LMI/OPS /ELEC/004 Issue:1 Rev :6 Dated: JAN18

3. SCOPE:

This LMI covers the Ni-Cd battery banks of various makes / types used for providing DC power supplies at NTPC Simhadri as per the Annexure-1.

4. REFERENCE DOCUMENT:

OD/OPS/ELEC/004 Issue-1 OCT 1994
OIN/OPS/ELEC/046 Rev:0 SEP 2009
OIN/OPS/ELEC/036 Rev:0 AUG 2007
OD/OPS/ELEC/004 Rev:1 APR 2019
OIN-OPS-ELEC-054 Rev:1 JAN 2021

5. REVISION DETAILS:

- The capacity test of battery banks should be carried out every 2 years with unit overhauling, earlier frequency of capacity testing was annually in Rev-1
- Annexure-V Help document for uploading battery capacity test data in SAP
- Annexure I,II,III modified as per new OD

6. PROCEDURE:

6.1 Battery Capacity Check

The capacity test shall be carried out Bi-Annually for battery banks mentioned in the Annexure-1.

Additionally, Surge capacity testing is to be done periodically on opportunity (short unit shut down) to ensure battery reliability mentioned in the Annexure-4.

- As the battery is already on float charge, the charger can be switched off and battery to be discharged at 0.2C5 till $1.0 \times n$ cell voltage. Record the capacity
- Re charge the battery at 0.2C5 A for 10 hours/ up to 1.72 Volts per cell @15 to 25° C for KPH type cells, whichever is earlier.
- Allow rest of 4 hours before discharging.
- Capacity Test will be carried out at C5 rating & all the cell voltages and total bank voltage will be recorded as per the format in Annexure-2.
- Individual cell voltage readings should be taken between respective posts of like polarity of adjacent cells, so as to include the voltage drop of the inter cell connectors
- The cells shall be discharged until the terminal voltage falls to 1.0 volts/cell or $1.0 \times n$ = total voltage for a battery bank. Where n = No. of cell.
- The measurement shall normally be taken hourly (0.2 C 5 discharging) but voltage shall be checked at 30 minutes' interval when the total battery voltage has fallen below $1.05 \times n$.
- Discharging of the battery bank is to be continued up to achieving of end voltage $1.0 \times n$, (do not stop the discharging on achieving 100% capacity).

Do not bypass or remove any cell during the discharge even if the voltage of lagging cells falls below 1.0 volts or reverse polarity is observed, however these weak cells can be identified and replaced by healthy ones later

- If during the capacity test any cell voltage falls below 1.0 V or cell polarity reversal takes place, the cell will not be disconnected, and the test will be continued till the total bank voltage reaches

V (modified) where

$V(\text{modified}) = (\text{No. of cells with correct polarity} \times 1.0) - (\text{Sum of reverse voltages}).$

- Temperature measurement to be done at fuses, joints during the discharge and boost charging of the batteries.
- Boost charge the batteries such that three consecutive readings of the cell voltage shows nearly same value.
- Capacity calculation= Amperes X Hours X Temperature correction.
(Temperature correction for +20°C to +45°C is 1.0).

% Capacity at 25°C with C5 rate = $(T_a / 5) \times 100 \times \text{Temperature correction}.$

where T_a = Actual time taken in hours to reach the end voltage of total bank (V_n)

Capacity Interpretation

Discharge Capacity	Battery Condition
Equal to & >100%	Good condition
90- 99.99%	Satisfactory condition
85-< 90%	Plan for replacement
< 85%	Replace the battery bank

- Normalize the battery & charger and connect to DCDB.

The replacement of battery banks shall be as per the table below:

S.No.	Battery Type	Replacement Criteria
1	Lead Acid - Tubular	Capacity 80 % or 10 years of service life whichever is earlier
2	Lead Acid -Plante	Capacity 80 % or 20 years of service life whichever is earlier
3	Nickel Cadmium	Capacity 85 % or 10 years of service life whichever is earlier

Instructions during Replacement of Total Battery Bank:

- The following procedure is to be followed for replacing the total battery bank after dismantling and removing the old battery bank

ELECTROLYTE FILLING:

- Flip open the top of the vent cap and remove the transport seal (plastic film).
- Do not completely remove the vent for filling the cells. Only flip open top of the vent cap for easy access to fill electrolyte.
- Fill the cells slowly with correct electrolyte as specified in Para 17.1 until the level reaches about 15 mm below the maximum level indication.
- Check the cells after 30 minutes and add electrolyte up to 10mm below max. level indication

CHARGING:

- Follow the procedure for first charging as given below.
 - (a) Charge at 0,2C5 A for 10 hours/ up to 1.72 Volts per cell @15 to 25° C for KPH type cells, whichever is earlier.
 - (b) Discharge at 0,2C5 A up to <1.0V/cell
 - (c) Charge at 0,2C5 A for 10 hours/ up to 1.72 Volts per cell @15 to 25° C for KPH type cells, whichever is earlier.
 - (d) Discharge at 0,2C5 A up to <1.0V/cell
 - (e) Repeat step (c) and (d) for another 2 cycles.
 - (f) Charge at 0,2C5 A for 10 hours

Give a rest of about 4 hours after completion of each charge & discharge. Adjust electrolyte level after completion of charge. After this final adjustment with electrolyte, ensure that the quantity of electrolyte in the battery is correct and battery is ready for service. For normal topping up, only DM/DI

water should be used, and no electrolyte shall be used. Please refer section 13.1.5 for capacity testing. During initial capacity testing during commissioning, cells shall deliver 100 % capacity or more.

Capacity Interpretation

Discharge Capacity	Battery Condition
Equal to & >100%	Good condition
90- 99.99%	Satisfactory condition
85-< 90%	Plan for replacement
< 85%	Replace the battery bank

7. RESPONSIBILITIES:

Instruction	Responsibility	Document Ref.
Job planning	MTP / AREAENGR	SAP SYSTEM
Job Execution	Area Maintenance Engr	EM/FILE No – DC/Capacity Test

The Area maintenance In charge shall be overall responsible for capacity test of batteries. UPS battery banks are maintained by CnI Department.

8. Fire Safety Precautions

The following fire safety precautions are to be taken in battery rooms

- a) In case of any fire / exigency the emergency EXIT should be available within close distance for safe escape.
- b) The Emergency EXIT should be well illuminated and pressurized so as to avoid smoke entry.
- c) All maintenance workforces shall be well trained for fire emergency drill.
- d) Ensure adequate number of arc flash suit of appropriate rating is available at site

9. NOTE ON BATTERY HEALTH MONITORING SYSTEM:

It is not applicable to the NTPC Simhadri station.

10. DOCUMENTS:-

The capacity test report will be prepared after the completion of capacity test of each battery bank, which shall include details of cells with reverse polarity, the actual capacity obtained during the test action plan for replacement of cells and/or details of weak cells replaced.

The following records are being maintained

Annexure-I checklist for capacity test data and replacement

Annexure-II format for battery capacity test report added.

Annexure-II-A format for surge load test report added.

Annexure-III format for recording battery capacity test

Annexure-IV Help document for uploading battery capacity test data in SAP

11. EXCEPTION REPORTING & DISPENSATION OF DEVIATION: -

Any deviation would be reported to Head of EMD

10. REVIEW: -

This LMI document will be reviewed once in every two years by Head of the Project, NTPC Simhadri.

ANNEXURE-1

Checklist for Battery bank capacity test and replacement

Sl. No	Location	Amp Hr rating	Make	Year of commissioning	Last capacity test	Service age	Replacement required(Yes/No)
1	SWYD 220V BANK-1	265AH	AMCO SAFT				
2	SWYD 220V BANK-2	265AH	AMCO SAFT				
3	U#1 220V BANK-1	990AH	HBL				
4	U#1 220V BANK-2	990AH	HBL				
5	U#2 220V BANK-1	990AH	HBL				
6	U#2 220V BANK-2	990AH	HBL				
7	U#3 220V BANK-1	990AH	AMCO SAFT				
8	U#3 220V BANK-2	990AH	AMCO SAFT				
9	U#4 220V BANK-1	990AH	AMCO SAFT				
10	U#4 220V BANK-2	990AH	AMCO SAFT				
11	SWYD 48V BANK-1	265AH	AMCO SAFT				
12	SWYD 48V BANK-2	265AH	AMCO SAFT				
13	U#1 24V BANK-1	990AH	SAFT URJA				
14	U#1 24V BANK-2	950AH	HBL				
15	U#2 24V BANK-1	950AH	AMCO SAFT				
16	U#2 24V BANK-2	950AH	HBL				
17	U#3 ST C&I 24V BANK-1	800AH	SAFT URJA				
18	U#3 ST C&I 24V BANK-2	800AH	SAFT URJA				
19	U#3 ST SG 24V BANK-1	530AH	HBL				
20	U#3 ST SG 24V BANK-2	515AH	HBL				
21	U#3 ST TG 24V BANK-1	670AH	HBL				
22	U#3 ST TG 24V BANK-2	670AH	HBL				
23	U#4 ST C&I 24V BANK-1	800AH	SAFT URJA				
24	U#4 ST C&I 24V BANK-2	800AH	SAFT				

25	U#4 ST SG 24V BANK-1	530AH	HBL				
26	U#4 ST SG 24V BANK-2	530AH	HBL				
27	U#4 ST TG 24V BANK-1	670AH	HBL				
28	U#4 ST TG 24V BANK-2	670AH	HBL				
29	U#3 ESP 24V B-1	540AH	AMCO SAFT				
30	U#3 ESP 24V B-2	540AH	AMCO SAFT				
31	U#4 ESP 24V B-1	540AH	AMCO SAFT				
32	U#4 ESP 24V B-2	540AH	AMCO SAFT				
33	AHP 24V B-1	225AH	AMCO SAFT				
34	AHP 24V B-2	225AH	AMCO SAFT				
35	CWPH 24V B-1	265AH	AMCO SAFT				
36	CWPH 24V B-2	180AH	AMCO SAFT				
37	FOPH S-1 B-1	250AH	AMCO SAFT				
38	FOPH S-2 B-1	85AH	HBL				
39	FOPH S-2 B-2	85AH	HBL				
40	CPU S-2 B-1	46AH	AMCO SAFT				
41	CPU S-2 B-2	30AH	HBL				
42	DM PLANT S-1 B-1	46AH	AMCO SAFT				
43	DM PLANT S-2 B-1	470AH	AMCO SAFT				
44	DM PLANT S-2 B-2	470AH	AMCO SAFT				
45	FWPH S-2 B-1	30AH	HBL				
46	FBPH S-2 B-1	30AH	HBL				
47	ASH SILO S-2 B-1	180AH	AMCO SAFT				
48	ASH SILO S-2 B-2	180AH	AMCO SAFT				
49	EDP S-1 24V B-1	57AH	AMCO SAFT				
50	ASH SILO S-1 AUG 220V B-1	12AH	HBL				
51	ASH SILO S-1 AUG 220V B-2	12AH	HBL				
52	ASH SILO S-1 AUG 24V B-1	85AH	HBL				
53	ASH SILO S-1 AUG 24V B-2	85AH	HBL				
54	ASH SILO S-2 AUG 220V B-1	12AH	HBL				
55	ASH SILO S-2 AUG 220V B-2	12AH	HBL				
56	ASH SILO S-2 AUG 24V B-1	85AH	HBL				

57	ASH SILO S-2 AUG 24V B-2	85AH	HBL				
58	ASH SILO S-1 24V B-1	54AH	HBL				
59	ASH SILO S-1 24V B-2	54AH	HBL				
60	SANKALP-2	85AH	HBL				
61	EDP S-2 24V B-1	46AH	AMCO SAFT				
62	Township 33KV Swgr 110V Btry Bank	155AH	HBL				
63	St#1 PLC, Control desk & RIO-1, RIO-2 (UPS 400V)	26AH	Exide Power Safe				
64	MCC-4 UPS, 400V (RIO-4 & RIO-3)	7AH	Chloride safepower				
65	WT-1 UPS, 192V	26AH	Exide Power Safe				
66	St#2 PLC UPS (400V)	100AH	AMCO SAFT				
67	SR#3 UPS (212V)	20AH	HBL				
68	SR#4 UPS (212V)	20AH	HBL				
69	St#1 HT swgr Battery Bank (220V)	188AH	AMCO SAFT				
70	St#2 HT swgr Battery bank (220V)	184AH	HBL				
71	St#2 PLC Battery bank (24V)	100AH	AMCO SAFT				
72	WT-1&2 24v Solenoid supply Battery bank	20AH	HBL				
73	MCC-2A Battery Bank (24V)	200AH	AMCO SAFT				
74	MCC-2B Battery Bank (24V)	170AH	AMCO SAFT				
75	MCC-2C Battery Bank (24V)	160AH	AMCO SAFT				

ANNEXURE-II

NTPC SIMHADRI
UNIT: _____
BATTERY BANK: _____

DATE: _____

DISCHARGE TEST REPORT

TIME											
HOUR		OC V	CC V	1	2	3	4	4.1 5	4.3 0	4.4 5	5.0 0
	S.N O.	VOLTAGE									
CELL TYPE	1.										
	2.										
	3.										
SP.GR.	4.										
	5.										
	6.										
CHARGE/ DISCHARGE Started on _____ at _____ hr s with _____ A _____ AH end voltage _V amb. Temp. starting ___C ending ___C electrolyte temp. starting ___C ending ___C	7.										
	8.										
	9.										
	10										
	11										
	12										
	13										
	14										
	15										
	16										
	17										
	18										
	19										
	20										

Time taken to reach the end voltage of the bank (Ta) =

No. of cells with reverse polarity =

No. of cells with reverse polarity before 90% of time duration =

No. of Cells replaced:

% Capacity Obtained at C5 Rate = $(Ta * 100) / 5$

ANNEXURE-II-A

SURGE LOAD TEST CHECKLIST

BATTERY BANK:	DATE:
Unit:	Location:
MAKE:	

DRIVE	TIME	VOLTAGE(V)	CURRENT(A)	TEMP READING OF MODULE

CHECKED BY:

WITNESSED BY:

Annexure-III Format for battery capacity test.

Cell No.	Cell Volt.	Sp. Gr.	Cell No.	Cell Volt.	Sp. Gr.	Cell No.	Cell Volt.	Sp. Gr.	Cell No.	Cell Volt.	Sp. Gr.
1			43			85			127		
2			44			86			128		
3			45			87			129		
4			46			88			130		
5			47			89			131		
6			48			90			132		
7			49			91			133		
8			50			92			134		
9			51			93			135		
10			52			94			136		
11			53			95			137		
12			54			96			138		
13			55			97			139		
14			56			98			140		
15			57			99			141		
16			58			100			142		
17			59			101			143		
18			60			102			144		
19			61			103			145		
20			62			104			146		
21			63			105			147		
22			64			106			148		
23			65			107			149		
24			66			108			150		
25			67			109			151		
26			68			110			152		
27			69			111			153		
28			70			112			154		

29			71			113			155		
30			72			114			156		
31			73			115			157		
32			74			116			158		
33			75			117			159		
34			76			118			160		
35			77			119			161		
36			78			120			162		
37			79			121			163		
38			80			122			164		
39			81			123			165		
40			82			124			166		
41			83			125			167		
42			84			126			168		
									169		

Reading taken by:

Reading reviewed by:

Area maint. Engineer

* 109 nos. cells for Lead Acid battery banks

** 169 nos. cells for Ni-Cd battery banks

Annexure-V Help document for uploading battery capacity test data in SAP

The following steps are to be followed to upload battery capacity test data in SAP.

01.	Use t_code IK07 to retrieve the measurement points from the system. Enter FL and select layoutCBM_ENTR and execute.
02.	Download the list as excel or directly copy (using Cntrl-Y & Cntrl-C) and paste first 4 columns of this layout into the first 4 columns of CBM upload format, i.e. in next sheet - "Format"
03.	Enter date & time in the format as indicated, in the columns E & F respectively.
04.	Enter the user ID of the person who has taken the readings in column G
05.	Enter the measured values in the column H.
06.	Leave the column I BLANK.
07.	Valuation code CM01 appears by default in column J. Change as applicable, but do not leave blank.
08.	Enter the remark in the column K. Then SAVE the excel file.
09.	COPY THE CELLS IN LIGHT BLUE COLOUR (COLUMN D TO COLUMN K) AND PASTE IN A TEXT FILE (NOTEPAD) AND SAVE.
10.	Login into SAP. Open t-code "ZPMCBM_UPLOAD". Browse this .txt file in the field "File Name".
11.	Press "Execute" to upload the data. After the uploading process is over, a report is displayed. Lines in the report - "Measurement Document <no.> created" indicate that the data has been successfully uploaded. In case of any other lines appear then the data will not be uploaded. Check the data or the format in that case.
12.	Check the uploaded data in the t_code IK17.

Data uploading Excel file

Microsoft Excel - NTPC-FS-PM-BDC-CBM

File Edit View Insert Format Tools Data Window Help

Type a question for help

Arial 10 B I U

Reply with Changes... End Review...

D32

Code to be entered from:
CM01: Acceptable
CM02: Watch list
CM03: Marginal
CM04: Unacceptable
CM05: Not applicable

SAP measurement point/counter no.

Date of taking reading

Time of taking reading

User ID of person recording the reading

Measurement point/Counter	Measurement date	Measurement time	Read by	Measurement point reading	Counter reading	Valuation code	Comments of CBM group	Keep blank for future use, if any)	Keep blank for future use, if any)
Num	Dats(yyyymmdd)	hh:mm:ss	User ID	Num		char	char		
POINT	DFDAT	DFTIM	DFRDR	READC	CNTRC	VLCD	MDTXT	DOCAF	PREST
5000018338	20080825	0:10:30	61942		200		abcdefg		
5000003058	20080825	14:10:30	61942		1115				
5000018337	20080824		61942		20				
5000003057	20080823	23:00:00	61942		1000				
5000018202	20080825	9:10:30	006634	905			xxxxxxxxxx		
5000018271	20080825	10:10:30	06634	5			yyyyyyy		
5000018283	25082008	2:10:30	6634	15					
5000018193	20080823		6634	6					
5000003060	20080825	18:00	6634	150		CM04	tttttt		

Sheet1

Ready

NUM

start

> Measureme...

SAP Logon 640

SAP Easy Acc...

New Microsof...

Microsoft Exc...

9:45 AM

Functional
Location
CHAR


Description of Meast.Pts.	Measure ment Position	Measurement point/Counter	Measurement date	Measureme nt time	Read by	Measur ement point readin g	Cou nter readin g	Valuati on code	Comme nts of CBM group char
CHAR		Num	Dats(yyyymmdd)	hh:mm:ss	User ID	Num		char	
TPLNR	TPTXT	POINT	DFDAT	DFTIM	DFRDR	READ C	CNTRC	VLCD	MDTXT
		5000018338	20080825	00:10:30	061942	8		CM01	OK
		5000003058	20080825	14:10:30	061942	8		CM01	OK
		5000018337	20080824	10:00:00	061942	3		CM01	OK
		5000003057	20080823	23:00:00	061942	7		CM01	OK
		5000018202	20080825	09:10:30	006634	905		CM01	OK, ON LOAD OK, DECOU PLED
		5000018271	20080825	10:10:30	06634	5		CM01	OK, ON LOAD OK, DECOU PLED
		5000018283	25082008	02:10:30	006634	15		CM04	HIGH ALARM
		5000018193	20080823	12:20:00	006634	6		CM03	OK
		5000003060	20080825	18:00:00	006634	150		CM01	OK

COS-ISO-00-

Preparing the file for converting in to text file

-All data should be left aligned.

-A to J columns and row up to 9 (in this case) should be selected.

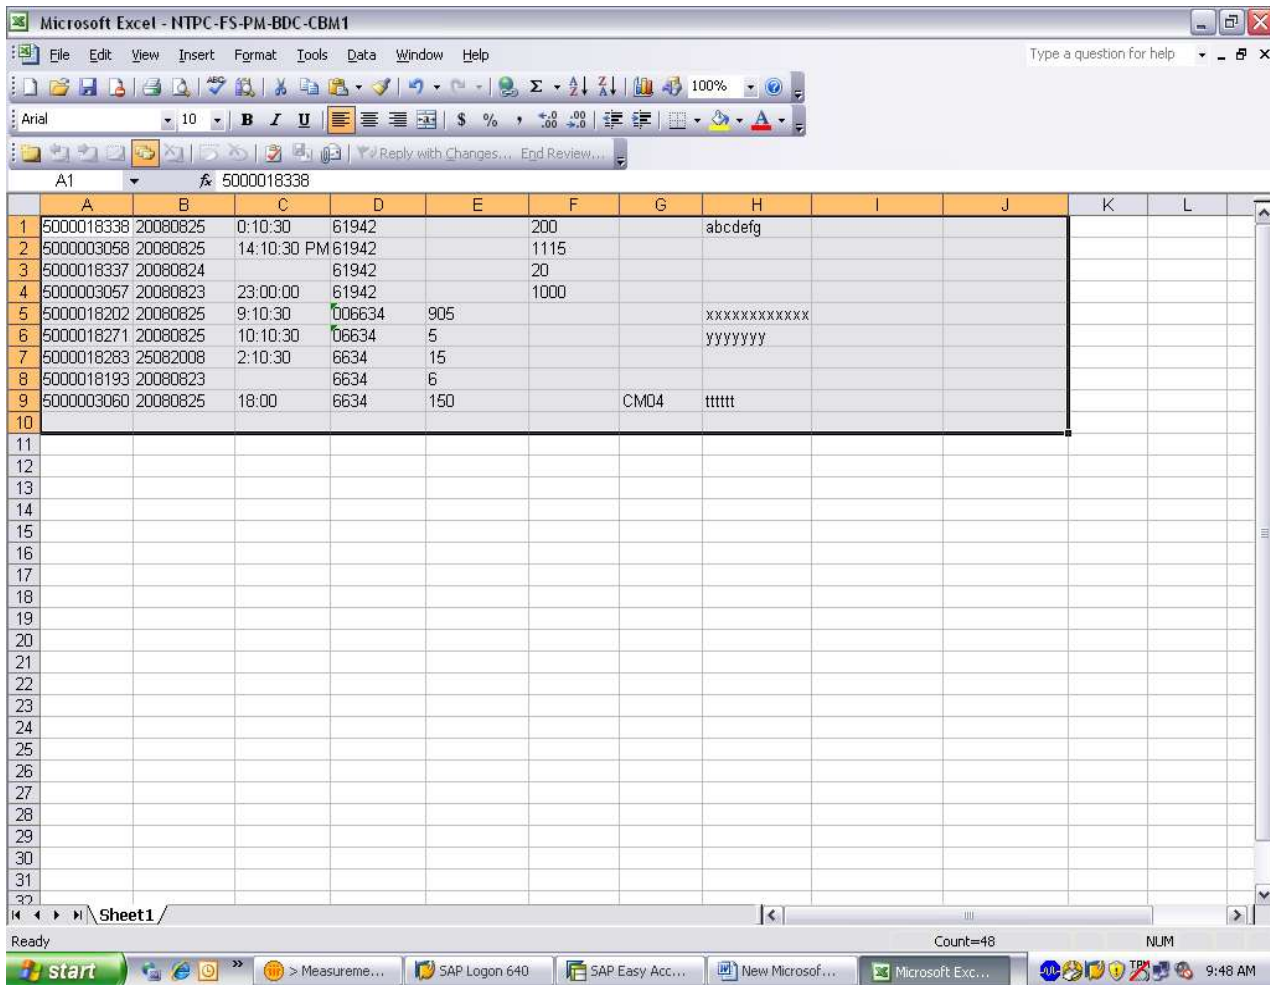

Microsoft Excel - NTPC-FS-PM-BDC-CBM1

Type a question for help

File Edit View Insert Format Tools Data Window Help

100%

Arial 10 B I U

Reply with Changes... End Review...


	A	B	C	D	E	F	G	H	I	J	K	L
1	5000018338	20080825	0:10:30	61942		200		abcdefg				
2	5000003058	20080825	14:10:30 PM	61942		1115						
3	5000018337	20080824		61942		20						
4	5000003057	20080823	23:00:00	61942		1000						
5	5000018202	20080825	9:10:30	06634	905			xxxxxxxxxx				
6	5000018271	20080825	10:10:30	06634	5			yyyyyyyy				
7	5000018283	25082008	2:10:30	6634	15							
8	5000018193	20080823		6634	6							
9	5000003060	20080825	18:00	6634	150		CMD4	tttttt				
10												
11												
12												
13												
14												
15												
16												
17												
18												
19												
20												
21												
22												
23												
24												
25												
26												
27												
28												
29												
30												
31												
32												

Sheet1

Count=48 NUM


Ready

start > Measureme... SAP Logon 640 SAP Easy Acc... New Microsof... Microsoft Exc... 9:48 AM

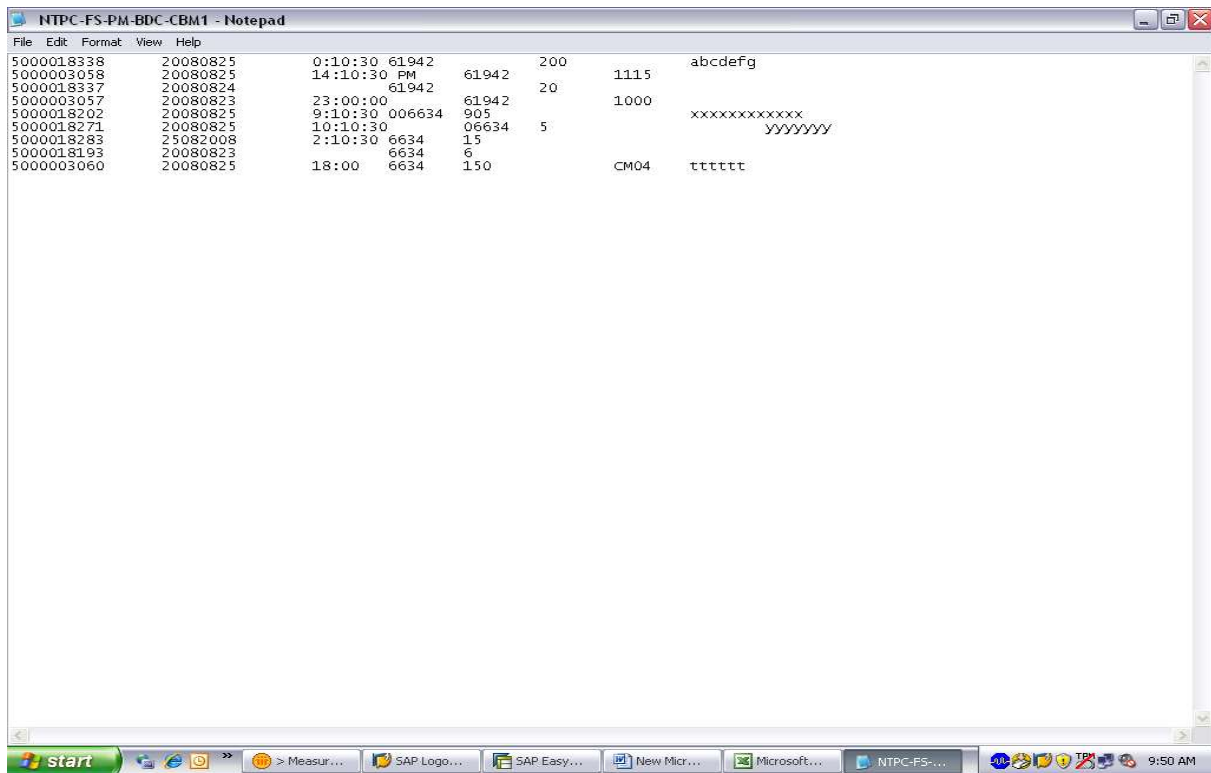Text file

```
File Edit Format View Help
5000018338 20080825 0:10:30 61942 200 1115 abcdefg
5000003058 20080825 14:10:30 PM 61942 20 1000
5000018337 20080824 61942 20 1000
5000003057 20080823 23:00:00 61942 905
5000018202 20080825 9:10:30 006634 5 xxxxxxxxxxxx
5000018271 20080825 10:10:30 06634 15 yyyyyy
5000018283 20080825 2:10:30 6634 6
5000018193 20080823 6634 150 CM04
5000003060 20080825 18:00 6634 150 CM04 tttttt
```

Use t-Code **zpmcbm_upload**

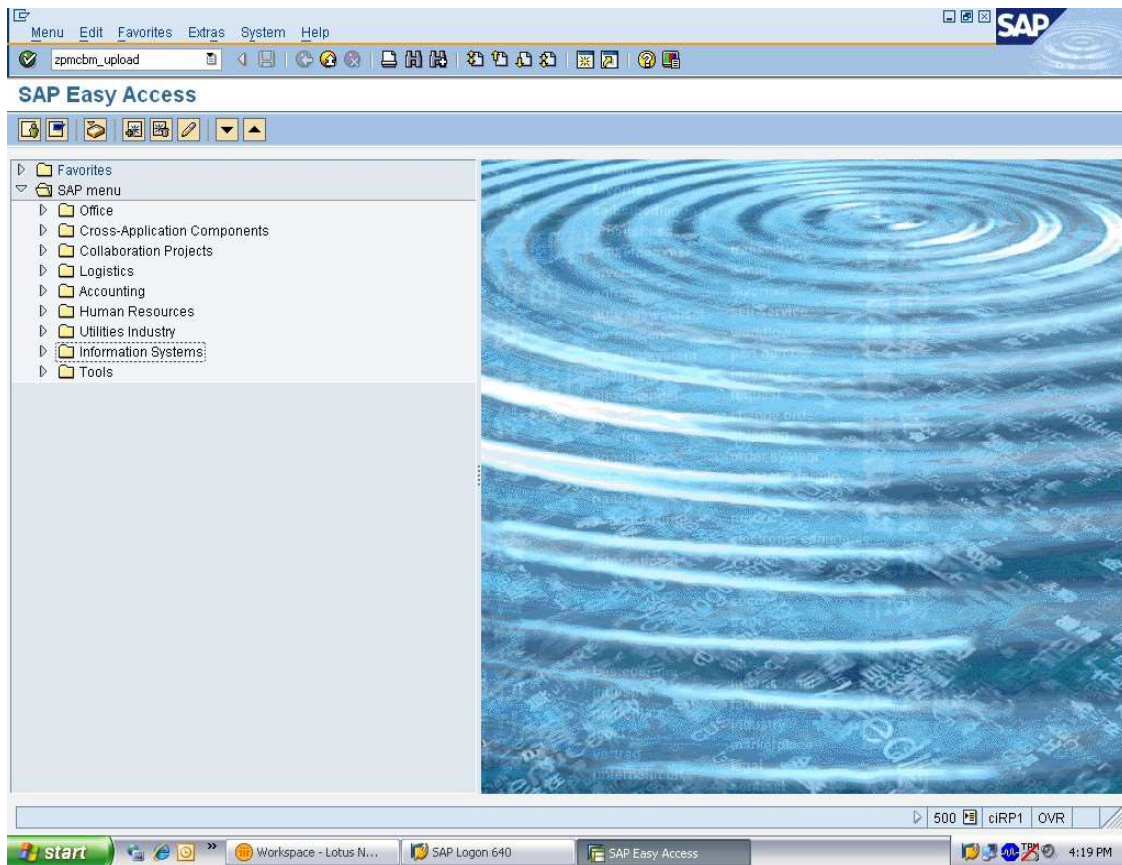

BDC screen where text file to be attached.

The screenshot displays the SAP BDC for Measurement Document Creation (IK11) screen. The interface includes a menu bar (Program, Edit, Goto, System, Help) and a toolbar. The main area contains the following fields and options:

- File Name:** A text field with a checkmark icon.
- Generate session:** A radio button option.
- Session name:** A text field.
- User:** A text field containing the value "004407".
- Keep session:** A checkbox.
- Lock date:** A text field.
- Call transaction:** A radio button option, which is selected.
- Processing Mode:** A text field containing the value "N".
- Update Mode:** A text field containing the value "L".
- Error sessn:** A text field.
- User:** A text field containing the value "004407".
- Keep session:** A checkbox.
- Lock date:** A text field.
- Nodata indicator:** A text field containing the value "1".
- Short log:** A checkbox.

The bottom status bar shows the text "ZPMCBM_UPLOAD | ciRP1 | OVR" and the system clock "12:22 PM".

Attached the file the from the source

The screenshot shows the SAP BDC for Measurement Document Creation (IK11) dialog box. The window title is "BDC for Measurement Document Creation (IK11)". The "File Name" field is set to "C:\Documents and Settings\Administrator\Desktop\New F...". The "Generate session" radio button is selected. The "Session name" field is empty. The "User" field is set to "004407". The "Keep session" checkbox is unchecked. The "Lock date" field is empty. The "Call transaction" radio button is selected. The "Processing Mode" field is set to "N". The "Update Mode" field is set to "L". The "Error sessn" field is set to "file name". The "User" field is set to "004407". The "Keep session" checkbox is checked. The "Lock date" field is empty. The "Nodata indicator" field is set to "I". The "Short log" checkbox is unchecked. The taskbar at the bottom shows the start button and several open applications: AK..., SA..., Wi..., Ma..., Bu..., Mi..., Me..., and BD... The system clock shows 12:14 PM.

Program Edit Goto System Help

SAP

BDC for Measurement Document Creation (IK11)

File Name C:\Documents and Settings\Administrator\Desktop\New F...

☐ Generate session

Session name

User 004407

Keep session ☐

Lock date

☒ Call transaction

Processing Mode N

Update Mode L

Error sessn file name

User 004407

Keep session ☒

Lock date

Nodata indicator I

Short log ☐

ZPMCBM_UPLOAD cIRP1 OVR

start AK... SA... Wi... Ma... Bu... Mi... Me... BD... 12:14 PM

Execute the BDC, data will be transferred to respective measurement point /counter.

Execute the

Program Edit Goto System Help

BDC for Measurement Document Creation (IK11)

File Name C:\Documents and Settings\Administrator\Desktop\New F...

☐ Generate session

Session name

User 004407

Keep session ☐

Lock date

☒ Call transaction

Processing Mode N

Update Mode L

Error sessn file name

User 004407

Keep session ☒

Lock date

Nodata indicator /

Short log ☐

ZPMCBI_UPLOAD cIRP1 OVR

start AK... SA... Wi... Ma... Bu... Mi... Me... BO... 12:14 PM

DISTRIBUTION LIST:

1. HOD (EM)
2. INTRANET
